


Fairfield / Vacaville Train Station and Peabody Road Improvements



Current Construction Status

APRIL 4 – 24, 2015

Work continues on the pedestrian underpass on the south side of the railroad tracks. Photo #1 (looking west) below shows the installed sheet piles that support the south side of the railroad tracks during construction. Photo #2 (looking north-west) displays the excavation work for the pedestrian underpass.

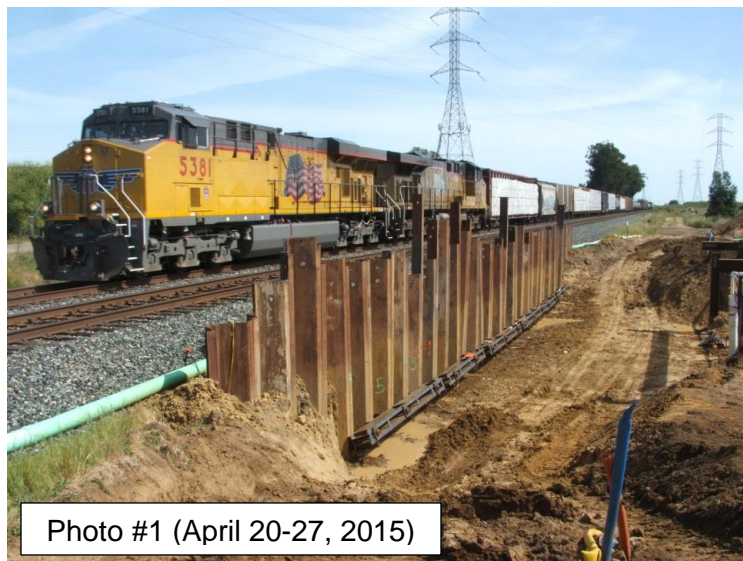


Photo #1 (April 20-27, 2015)



Photo #2 (April 20-27, 2015)

MARCH 12 – 27, 2015

The Contractor and CM Team continue to coordinate with the various utility companies to locate all below ground utilities within the vicinity of the south pedestrian underpass. Photo #1 (taken on the south side of the railroad tracks looking west) displays the support system constructed by the contractor for the existing fiber optic conduit to remain.



March 12, 2015

Great news! The City has issued the official Notice to Proceed to the contractor Teichert / Myers JV. The contractor this week worked on the environmental fencing, storm water protection devices, establishing dewatering systems, and install sheet piles for the new pedestrian undercrossing. Our project team continues to meet each week and pushing forward with submittal, contract clarifications, and shop drawing reviews. The railroad (UPRR) and its representatives have continued to partner with us on this important project for the community.



February 2-8, 2015

During the first week of February, Kinder Morgan removed sections of an abandon pipeline to make room for the new bridge footings. In addition, construction offices have been installed near the site in preparation of field personnel.

